

perc quickMCEF-200
Rev: 4/07Mineral County Health Department
Application for Individual On-site Sewage Evaluation304-288-1321 Health Dept
Denny Tidgell
Name JEFFREY A METCALF Phone 304-813 9298Address RT 1 Box 1276 BURLINGTON WV 26710Property Location RT 46 TOWARDS FORT AUBRY FOREBACK RD ON LEFT
1-MILE ON LEFT TOP OF HILLProperty Deed Recorded in: Book No. 263 Page 645 Date Recorded 3/15/91County Tax Map _____ Parcel Number _____ Size of Lot 7 + ft² (acres)

Application is hereby made for a site investigation to determine the suitability of the subject property as a site for the small sewage system indicated below:

☒ Septic System ☐ Pit Privy ☐ Vault Privy ☐ Other _____

The results of a percolation test conducted in accordance with the requirements of Legislative Rule 64-17 "Individual and On-Site Sewage Systems (Excerpts)" follows:

Depth of test holes: #1 24", #2 24", #3 24", #4 24"Time for water to fall six (6) inches in test hole #1 20 minutes#2 35 minutes#3 45 minutes#4 30 minutesTotal 130 minutes divided by 24 = 5.41 minutes/inch


A test hole bored or dug six (6) feet deep () is () is not free of water or solid rock.

Percolation test conducted by: Name JEFFREY A METCALFAddress RT 1 Box 1276 BURLINGTON WV 26710Signature Jeffrey A Metcalf Date 7-12-13A place is provided on the back of this page for a plot layout showing the property lines and relative locations of buildings, water supplies, percolation test holes, six foot hole, and other pertinent features. Parcels less than two (2) acres must show precise location of 10,000 square foot reserve area.I (we), the undersigned, certify that the information contained herein is correct and accurate to the best of my (our) knowledge. It is further understood that this form is not an application for a permit, and subsequent acceptance of this site by the Mineral County Health Department does not constitute a permit to install a sewage system.Owner's signature Jeffrey A Metcalf Date 7-12-13

Plot Layout

In the space below provide a plot layout showing the property lines and relative locations of buildings, water supplies, percolation test holes, six foot hole, and other pertinent features. Parcels less than two (2) acres must show precise location of 10,000 square foot reserve area.

☒ House -x- Water Supply Line ⊗ Water Supply ||||| Trees (P) Percolation Test Site [ST] Septic Tank
 ----- Soil Absorption Line → Direction of Ground Slope _____ Property Line [MH] Mobile Home

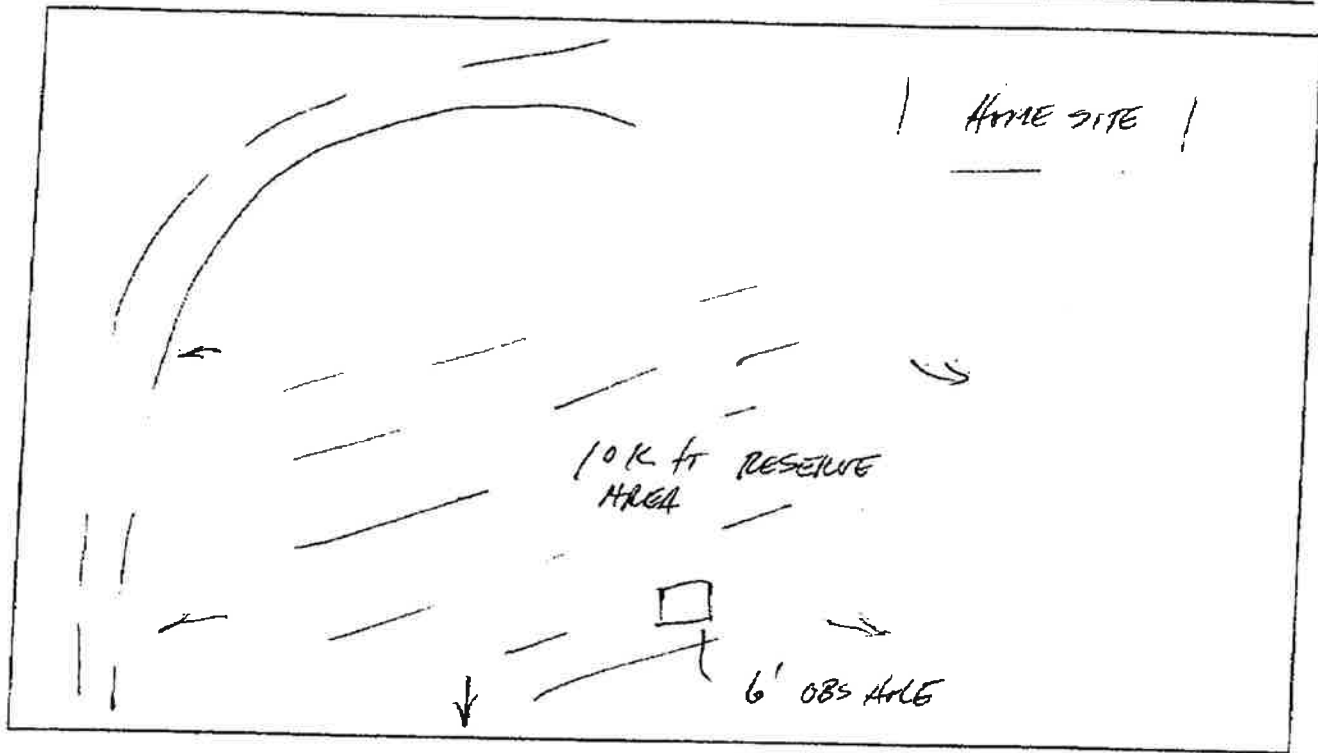

FOR HEALTH DEPARTMENT USE ONLY

Date Received	Date Site Evaluation	Reviewed by	Date Fee Paid	Received From
7-12-13	7-12-13	J. Schute	7-12-13	J. METCALF

6' Excavation Observed	Reserve Area Location (GPS Coordinates)	Drainfield Design		
		Depth	ft ² of Trench Area	Trench Separation
48" LOOSE SAND/SILT 48" → BOTTOM RIGHT SAND/CLAY/2014 DRY	39 28 .2 78 49 21.4	24" MAX	400 ft ² / BR.	6'

Comments: CL I SYS TO BE OVERSIZED DUE TO TIGHTNESS AT 48"

This is to certify that the Mineral County Health Department reviewed the contents of this form and conducted a site visit on the subject property. Based on the information provided it appears that the site () is () is not suitable for the installation of the small sewage system indicated.

Signature

Jason J. Schute

Date

7-12-13
