

Rev 2/11

ST/CO USE ONLY DATE RECEIVED MM DD YY		DATE THE WELL WAS COMPLETED MM DD YY <u>7 24 2012</u> PERMIT NO. DW- <u>14-12-082</u>		West Virginia Department of Health and Human Resources BUREAU FOR PUBLIC HEALTH WATER WELL COMPLETION REPORT		FORM SW-258 THIS REPORT MUST BE SUBMITTED WITHIN 30 DAYS AFTER WELL IS COMPLETED FILL IN THIS FORM COMPLETELY PLEASE PRINT OR TYPE															
LOCATION OF WELL Well Owner: Last Name <u>Kesner</u> First Name <u>JOHNNY & CECELIA</u> Street/Road <u>FOX HOLLOW RD.</u> County <u>HAMPSHIRE</u> Zip Code _____																					
Latitude: _____ Deg _____ Min _____ Sec Longitude: _____ Deg _____ Min _____ Sec Acquired By: ☐ GPS ☐ Topo ☐ Other				AREA NAME/LOCATION: <u>HIDDEN HOLLOW</u> <u>LOT 1</u>		TYPE OF WELL: ☒ Potable ☐ Public Water Supply ☐ Geothermal ☐ Industrial ☐ Commercial ☐ Dewatering ☐ Irrigation ☐ Test/Exploratory ☐ Other															
WELL LOG <table border="1" style="width:100%; border-collapse: collapse;"> <thead> <tr> <th colspan="2">Depth</th> <th rowspan="2">State the kind of formation penetrated, their color, caves, and if water bearing with estimate flow (GPM).</th> </tr> <tr> <th>From (ft.)</th> <th>To (ft.)</th> </tr> </thead> <tbody> <tr> <td>0</td> <td>33</td> <td>Brown shale</td> </tr> <tr> <td>33</td> <td>400</td> <td>Gray shale</td> </tr> <tr> <td>337</td> <td>338</td> <td>water - 1 1/2 GPM</td> </tr> </tbody> </table>				Depth		State the kind of formation penetrated, their color, caves, and if water bearing with estimate flow (GPM).	From (ft.)	To (ft.)	0	33	Brown shale	33	400	Gray shale	337	338	water - 1 1/2 GPM	DRILLING METHOD ☐ Cable Tool ☐ Rotary ☒ Rotary Hammer ☐ Other Hole Diameter <u>6</u> (in) Total depth <u>400</u> (ft) CASINGS RECORD MAIN CASING TYPE ☒ Steel ☐ Plastic ☐ Other Casing Diameter <u>6 5/8</u> (in) Wall Thickness <u>.188</u> (in) Casing Length <u>60</u> (ft) Other Casing or Liner Used ☐ Steel ☐ Plastic ☐ Other Casing/Liner Diameter _____ (in) Length _____ (ft) from _____ (ft) to _____ (ft) SCREEN RECORD ☒ Not Installed ☐ Installed Material: ☐ Bronze ☐ Plastic Diameter of screen _____ (in) Slot size _____ Length _____ (ft) from _____ (ft) to _____ (ft) GRAVEL PACK RECORD Gravel Pack: ☐ Yes ☒ No From _____ (ft) to _____ (ft)		GROUTING RECORD Grouting Material: ☐ Cement ☒ Bentonite Clay Other _____ No. of Bags: <u>3</u> Installation Method: <u>PUMPED</u> PUMP INSTALLED By Driller ☐ Yes ☐ No ESTIMATED WELL YIELD Estimated at <u>1 1/2</u> G.P.M. Static Water Level <u>40</u> (ft) *Pumping level below land surface <u>398</u> (ft) after <u>1</u> hrs. at <u>1 1/2</u> G.P.M. (Estimated) *Note: For Public Water Supply wells please submit required yield and drawdown tests.	
Depth		State the kind of formation penetrated, their color, caves, and if water bearing with estimate flow (GPM).																			
From (ft.)	To (ft.)																				
0	33	Brown shale																			
33	400	Gray shale																			
337	338	water - 1 1/2 GPM																			
I hereby certify that this well has been constructed in accordance with state rules and in conformance with all conditions stated in the above captioned permit, and that the information presented herein is accurate and complete to the best of my knowledge.				WELL HEAD COMPLETION Casing height above grade <u>1</u> (ft) Type Of Well Cap _____ Installed: _____ VARIANCE ISSUED ☐ Yes ☐ No Request Number _____ COMMENTS BY INSTALLER:																	
Company Name <u>B.W. SMITH WELL DRILLING</u> WV Contractor No. <u>038905</u> Business Registration No. <u>1005-5395</u> Master Well Driller Certification No. <u>574</u> Master Well Driller (print) <u>Chris Wolford</u> Master Well Driller Signature <u>Chris Wolford</u>																					
SITE SUPERVISOR (SIGNATURE OF DRILLER OR JOURNEYMAN RESPONSIBLE FOR SITEWORK IF DIFFERENT FROM MASTER DRILLER.) Journeyman Well Driller Certification No. _____ Journeyman Well Driller (please print) _____ Apprentice and Name (s) _____																					

Hampshire County Health Department On-Site Sewage Disposal System Inspection Form

Permit # **ST-14-13-03**

Name of Owner: Johnny & Cecelia Kesner Installer: Walter Fields
Address: 185 N. Bolton Street, Romney, WV 26757
Property Location: Hidden Hollows Lot 1 Lot Size: 29.1524 acres Acres
Type of Facility: new Facility is: ☒ New ☐ Existing
Design Loading in gpd/# Bedrooms: 3 Source of Water: well

SEWAGE TANK COMPONENT

Capacity in Gallons: 1000 Material: precast concrete
Distances (in feet) of Tank to: Dwelling NA
Private ☒ Public ☐ Water Source: NA Property Line: >100

ON-SITE DISPOSAL SYSTEM

Class I Systems: Standard Soil Trenches () or Bed () Gravelless Pipe (), Diameter In.
Chamber Soil Absorption Trenches (☒) or Bed ()
Class II Systems: Pumped/Dosed Soil Absorption Trenches () or Bed () LPP ()
Evapotranspiration Trenches () or Bed ()
Shallow Soil Absorption Trenches () or Bed () Other:

No. of Lines: 3 Length (in feet): 80's
Width of Trenches: 36 inches/feet Depth to Bottom of Field: 24 inches
Size Equates to 1200 sq ft of SGF
Distance (in feet) of System to: Dwelling NA
Private (x) Public () Water Source: NA Property Line: >100
Remarks: house and well not constructed at time of inspection
GPS: N39 30 11.2 W78 31 40.3

An inspection indicates that
The sewage disposal system
Described above
DOES MEET ☒


DOES NOT MEET ☐ or
**CANNOT BE DETERMINED TO
MEET ☐** the minimum standards
Established by the West Virginia
Bureau of Public Health.

To correct a health hazard,
Modifications to existing systems
May be done to improve part of a
System. Such modifications may
Not be able to be designated as
a Does meet system since
Inadequate information is known.

Although many factors
Contribute to the successful
Functioning of a sewage disposal
System, this office recommends
Water conservation and
Maintaining an even usage of
Water throughout the week.

Visit Date(s): 7/23/2012

FINAL INSPECTION DATE: 7/23/2012

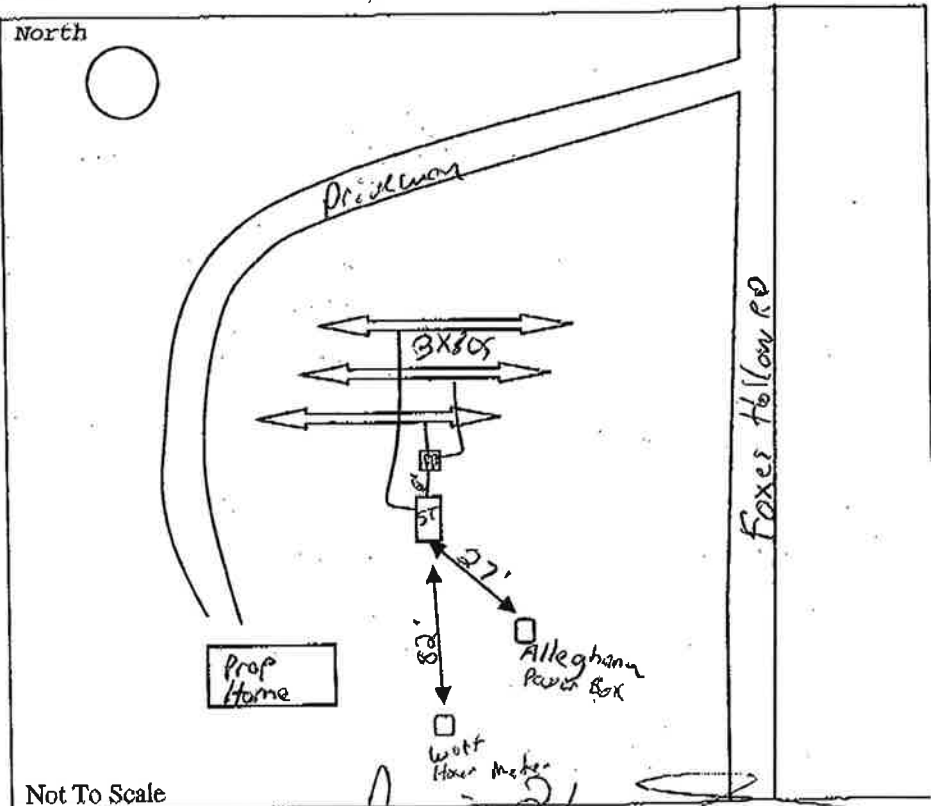

SANITARIAN: Dennis H. H.
